

# SVSD 2015 Bond Program

## Elementary #6 Progress Status Report

---

Date: October 23<sup>rd</sup>, 2015  
To: Ryan Stokes  
Copy: Carolyn Malcolm, Joel Aune  
From: Clint Marsh  
Subject: **October 23rd Current Progress Status**

---

Week October 16<sup>th</sup> to October 23<sup>rd</sup>, as follows:

### New:

#### **Phase 2 - Building Construction**

- Classroom Wings - ~~East, North, and South~~ **Revised** South, East, North Construction has begun:
  - Spray on waterproof membrane/footing insulation has been installed in the **East and South Wing**.
  - Under-slab roll out sheet waterproof membrane installation, footing seal integration, and seam sealing **complete in the East Wing and In Process at South Wing**.
  - On-site exterior wall pre-fabrication is **complete for the East Wing and starting for South Wing**.
  - Exterior footing drain installation is **complete in the East Wing and heading around South Wing**.
- **Batter boards continue to be installed for footing layout for Hallway, Administration, and Gym Wing.**
- **All under-slab water, sewer, fire, electrical, data, piping and wire conduits are being installed throughout.**

### Previous Relevant Status Items:

- Planning, Education Specifications, Design, Permitting, Tree Harvesting, Stump Grinding, Silt Fence Installation, Off-Site Hauling Operations, Rock/Gravel Haul-In Operations, Sanitary Sewer, Storm Drainage, Water System, On-Site Surface Water Sediment Pond, Building Slab, Parking Lots, Playgrounds, Slope Sub-Grades, Water Connection to City System, transition from the Phase 1 to Phase 2 contractor, on-site processing of topsoil, crushed rock sub-base and asphalted treated base in the entry, parking lots, exit, on-site gravel work access roads, slope protection, and playfields have all been completed.

### Future Activities:


- Digging out the remaining building footings.
- Forming the concrete footings, foundations, stem walls, throughout.
- Pouring concrete into the building footing forms.
- Installing all associated plumbing, mechanical, electrical, and data infrastructure.
- Installation of vapor/water barrier under slab sheet membrane and spray on stem wall membrane.
- Pouring of concrete slabs.
- Pre-fabrication of exterior walls.
- Installation of exterior walls.
- Concrete curb construction where possible.
- Exterior footing drains around the entire building.

### Attachments:

10-21-2015 Progress Photos

**Snoqualmie Valley SD No. 410 -  
New Elementary #6**

**Pictures Taken: 10/20 & 21/2015  
Progress Photographs**

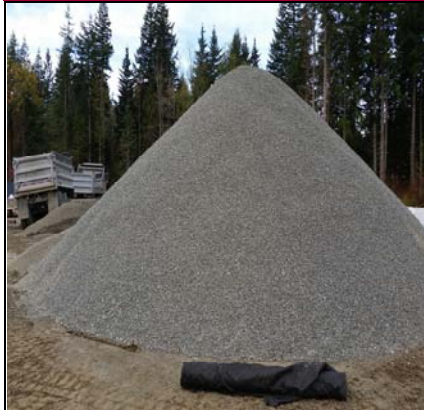

Crushed Rock Ready For Under The Slab



More Under-Slab Ready For Crushed Rock



More Waterproof Membrane Installing



More Forms Being Pulled From Footings



Steel Column Footings For HVAC Mezzanine



More Form Base Cleats - One At A Time



Measure Twice Cut Once - More Layout



More Footings - Forms And Rebar



Conduit Prepared For Waterproofing



Color Coded Conduit - Room By Room



Concrete Slab Ready For Exterior Walls



Exterior Walls Ready For A Concrete Slab
