

Mount Si High School Replacement Progress Status Report

Date: September 16th, 2016
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **September 16th Current Progress Status**

Weeks prior to September 16th, as follows:

New:

- **Permit Process Completion:**

- **SEPA - State Environmental Policy Act**
- **City Design Review Approval**
- **Conditional Use Permit**
- **Shoreline Conditional Use Permit**
- **NPDES Storm/Surface Water Permit**
- **Individual Permits For The Following Projects:**
 - Demolition Projects**
 - Seven (7) Newly Acquired Houses
 - Start June 1st, 2016 / Completion July 1st, 2016 - **Completed**
 - Baseball/Softball Fields Demolition
 - Start June 15th, 2016 / Completion July 1st, 2016 - **Completed**
 - Portable Wing Foundation Demolition
 - Start July 1st, 2016 / Completion July 15th, 2016 - **Completed**
 - Relocation Projects**
 - MSHS Portable Wing To Freshman Campus
 - Start June 23rd, 2016 / Completion August 31st, 2016 - **Completed**
 - TLC Portable To New Property Location
 - Start September 15th, 2016 / October 15th, 2016 - **In Process**
 - Site Development Projects**
 - Temporary Parking Lot Construction
 - Start September 15th, 2016 / Complete November 15th, 2016 - **In Process**
 - New MSHS Building Pad Construction
 - Start November 15th, 2016 / Completion January 15th, 2017 - **In Process**
 - New Construction Projects**
 - MSHS Two Double-Wide Temporary Portables
 - Start September 15th, 2016 / Completion November 1st, 2016 - **In Process**

Previous Relevant Status Items:

- Planning, Visioning, Education Specifications, Schematic Design, Design Development...

MSHSRP - September 16th Current Progress Status - Continued

Future Activities: - Finalization and Completion of Construction Documents

- **Phase 0 Building Pad Construction**


- Silt Fence Installation
- Off-Site Hauling Operations
- Rock/Gravel Haul-In Operations

- **Stone Column Sub-Grade Construction**

- Start December 5th, 2016 / Completion July 31st, 2017 - **Pending**

- **New High School - Phase One and Two Building Permit**

UPCOMING CONSTRUCTION AREAS BEGINNING WORK SEPTEMBER 19TH, 2016
PLEASE USE CAUTION ON MEADOWBROOK AS TRUCKING OPERATIONS BEGIN
TRAFFIC CONTROLS WILL BE IN OPERATION WEDNESDAY SEPTEMBER 21ST, 2016

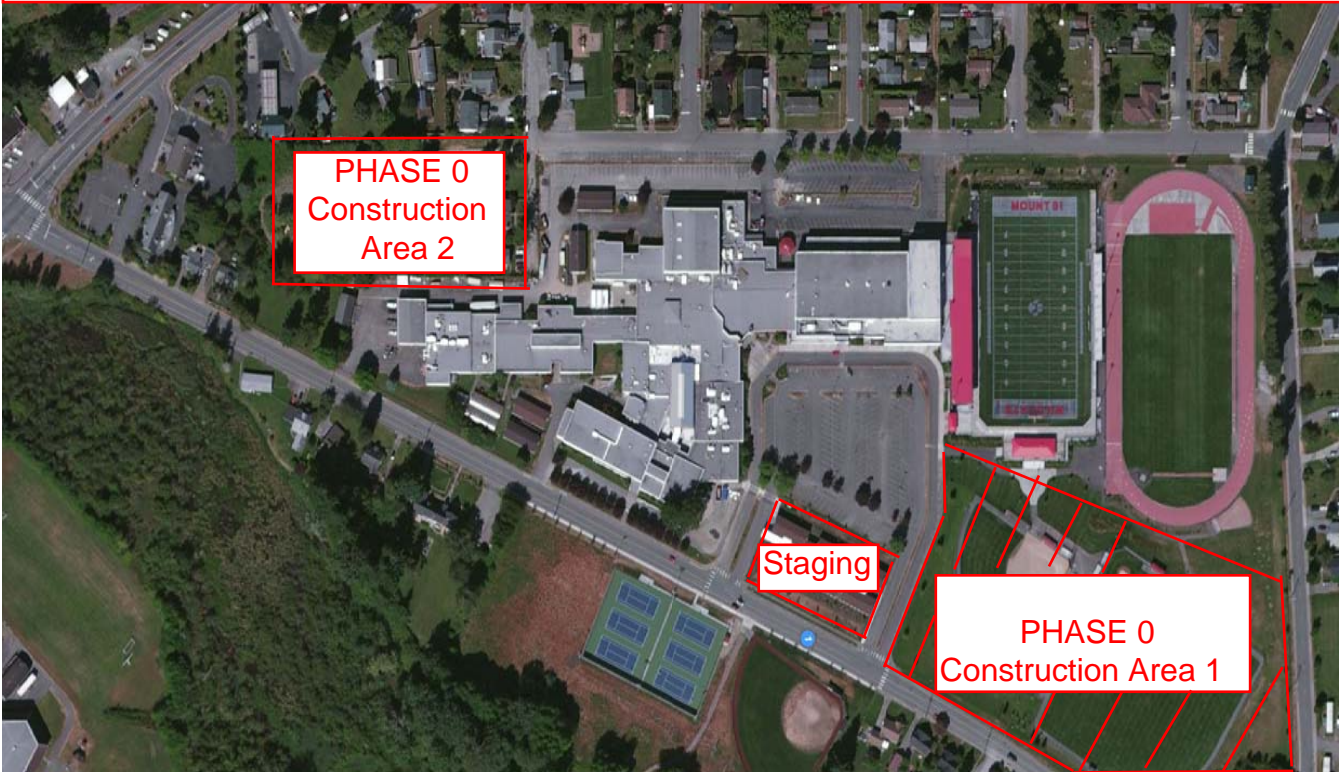

Attachments:

Progress Photos - Pending
