

SVSD 2015 Bond Program

Mount Si High School Replacement Progress Status Report

Date: January 15th, 2017
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **January 15th Current Progress Status**

Weeks from December 15th to January 15th, as follows:

New:

- **Temporary Parking Lot Construction**
 - **Opened December 30th - Complete**
- **Phase 0 Building Pad Construction**
 - Curbing/Gutters/Sidewalks Removed
 - Existing Asphalt Paving Ground Into Gravel
 - Off-Site Hauling Operations For Remaining Pad Area Continues
 - Rock/Gravel Haul-In Operations For Remaining Pad Area Continues
- **Stone Column Sub-Grade Reinforcement**
 - Stone Column Construction Continues With Both Crane/Probe Installation Rigs
 - Off-Site Hauling Operations For Limited Soil Removal Continues
 - Rock/Gravel Haul-In Operations For Remaining Stone Columns Continues
- **Finalization and Completion of Construction Documents**
 - Construction Documents Complete
 - Constructability Review Complete

Previous Relevant Status Items:

- Planning, Visioning, Education Specifications, Schematic Design, Design Development, Ten Development Permits (as listed in the September 16th Status Report), Initial Demolition Projects Complete, Relocation of the Twelve Classroom Portable Wing and TLC Portable, Installation of the Two Double-Wide Temporary Portables, Silt Fence Installation, Surface Water Management Structures Installed, Temporary Perimeter Fencing Installed, Trucking Haul Roads Constructed, Crane/Probe Assemblies Complete, Temporary Parking Lot Constructed...


Future Activities: - Phase One and Two City Building Permit - Continues Under Review

- Phase One and Two General Contractor Bid Process - January 24th thru March 7th, 2017

Attachments:

Progress Photos - December 2016 & January 2017


Snoqualmie Valley SD - Pictures Taken: Dec 2016/Jan 2017 -Various Times Mount Si High School Replacement Project - Phase 0 Progress Photographs

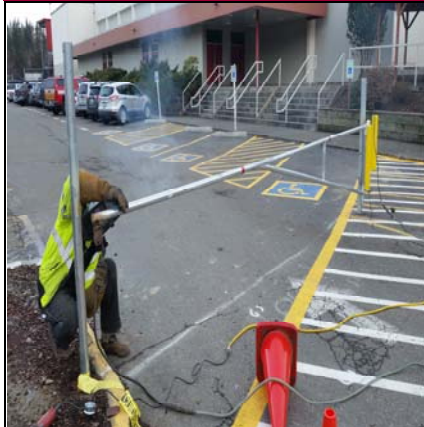

Temp Parking Lot Receives Safety Gates



Front Parking Lot Ground Into Gravel 1

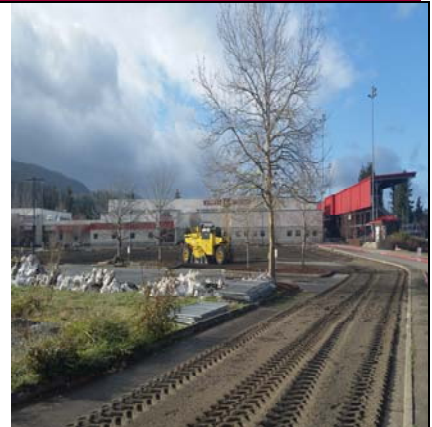

Front Parking Lot 2



Front Parking Lot 3



Front Parking Lot 4



Concrete Sidewalk Demolition




More Stone Column Installations



Bringing Down The Existing Grade



Hauling Out More Soil

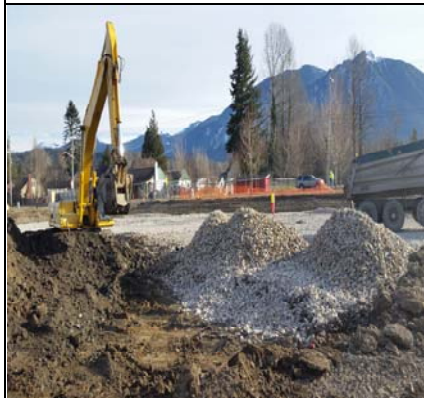

Bringing In More Rock



Bringing Grade Down Even More For Rock



More Rock Pad For Stone Column Rigs
