

SVSD 2015 Bond Program

Mount Si High School Replacement Progress Status Report

Date: November 15th, 2016
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **November 15th Current Progress Status**

Weeks from October 24th to November 15th, as follows:

New:

- **Phase 0 Building Pad Construction**
 - Off-Site Hauling Operations
 - Rock/Gravel Haul-In Operations
 - ***Suspended PENDING Relocation of Automobiles To Back Temporary Parking Lot***
- **Temporary Parking Lot Construction**
 - Off-Site Hauling Operations
 - Rock/Gravel Haul-In Operations
 - Storm Drainage Pond Construction
 - Underground Drainage Utility Construction
- **Stone Column Sub-Grade Reinforcement Submitted For City Permit - Continues Under Review**

Previous Relevant Status Items:

- Planning, Visioning, Education Specifications, Schematic Design, Design Development, Ten Development Permits (as listed in the September 16th Status Report), Initial Demolition Projects Complete, Relocation of the Twelve Classroom Portable Wing and TLC Portable, Installation of the Two Double-Wide Temporary Portables, Silt Fence Installation, Surface Water Management Structures Installed, Trucking Haul Roads Constructed...

Future Activities: - Temporary Parking Lot

- **Crushed Rock Surface Installation**
- **Parking Stall Wheel Stop Installation**
- **Bus Loop Crushed Rock Construction**
- **Bus Loop Asphalt Installation**

- Stone Column Sub-Grade Construction

- Start December 5th, 2016 / Completion July 31st, 2017 - **Pending**

- Finalization and Completion of Construction Documents

- Phase One and Two City Building Permit - Continues Under Review

- Phase One and Two General Contractor Bid Process

Attachments:

Progress Photos - October & November 2016


Snoqualmie Valley SD Pictures Taken: Oct & Nov - 2016 -Various Times
Mount Si High School Replacement Project - Phase 0 **Progress Photographs**



Back Lot - "Wettest October On Record"...



1 of 2 Temporary Storage Ponds Installed

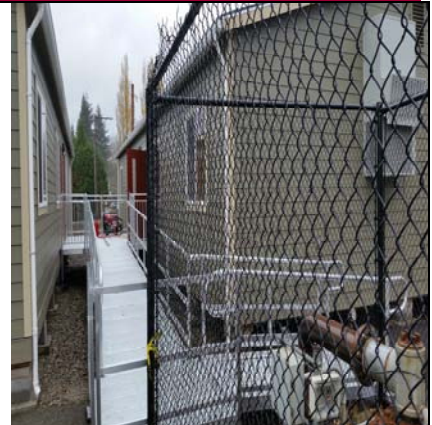

New Portables Access Ramps Installed



Portable Interior Finishes In Process



Trucks Importing Large Base Rock



Temporary Parking Lot Base Rock Start



Base Rock Installation Continues



Drainage Pipe & Catch Basins Delivered



2 of 2 Temporary Storage Ponds Installed



Pipe To Vault Structure Connections 1



Pipe To Vault Structure Connections 2



Backfilling And Sealing For Coming Rock
