

SVSD 2015 Bond Program

Mount Si High School Replacement Progress Status Report

Date: March 15th, 2017
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **March 15th Current Progress Status**

Weeks from February 15th to March 15th, as follows:

New:

- **Phase 0 Building Pad Construction**

- Construction Of Permanent And Temporary Sewer, Water, Storm Drainage Continues
- Off-Site Hauling Operations For Remaining Pad Area Continues
- Rock/Gravel Haul-In Operations For Remaining Pad Area Continues
- Site Development Contractor Remains On Schedule And Is Nearing Completion

- **Stone Column Sub-Grade Reinforcement**

- Stone Column Construction Continues With Both Small & Large Crane/Probe Installation Rigs
- A "Vibro-Cat" Probe (No Crane Required) For Liquefaction Structural Columns Continues In Service
- Off-Site Hauling Operations For Limited Soil Removal Continues
- Rock/Gravel Haul-In Operations For Remaining Stone Columns Continues
- Stone Column Contractor Slightly Ahead Of Schedule And Approximately 60% Complete

- **Phase One And Two General Contractor Bid Process Continues**

- Bid Opening Held March 7th, 2017
- Spee West Construction Is The Phase One & Two General Contractor

Previous Relevant Status Items:

- Planning, Visioning, Education Specifications, Schematic Design, Design Development, Ten Development Permits (as listed in the September 16th Status Report), Initial Demolition Projects Complete, Relocation of the Twelve Classroom Portable Wing and TLC Portable, Installation of the Two Double-Wide Temporary Portables, Silt Fence Installation, Surface Water Management Structures Installed, Temporary Perimeter Fencing Installed, Trucking Haul Roads Constructed, Crane/Probe Assemblies Complete, Temporary Parking Lot Constructed, Old Parking Lot Demolished, Construction Documents and Constructability Review Complete, Bid Process Complete...

Future Activities: - Phase One and Two City Building Permit - Continues Under Review

- Phase One and Two General Contractor Mobilization On Site

Attachments:

Progress Photos - February 2017 & March 2017

**Snoqualmie Valley SD - Pictures Taken: Feb/Mar 2017 -Various Times
Mount Si High School Replacement Project - Phase 0
Progress Photographs**



Temporary Retaining Wall & Drainage



Temporary Sewer Line Encased In Concrete



Temporary Sewer Manholes For Phase 1



Permanent Water Line For Phase 1



New Water Main Valves For Phase 1



Backfilling Temporary Retaining Wall




Another Retaining Wall Layer Of Block



Continuing North With The Retaining Wall



Drilling & Probing Structural Columns

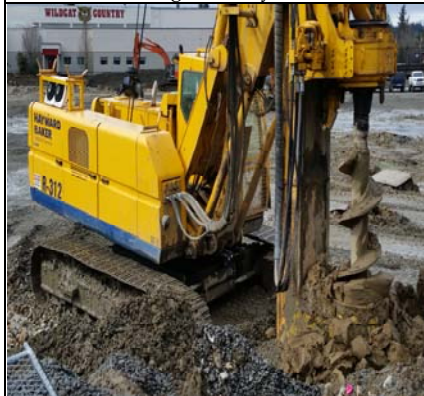

Close Up Of Pilot Hole Drilling



All Stone Column Rigs Running



...If It's Not Rain It's More Snow...
