

SVSD 2015 Bond Program

Timber Ridge Elementary Progress Status Report

Date: August 12th, 2016
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **August 5th Current Progress Status**

Week August 5th to August 12th, as follows:

New:

Phase 2 - Building Construction

- In keeping with the TRES Dendrochronology Theme the Seven Hundred Year Old Feature Log arrived and is being installed In the Entry Hallway - ***What do you know about the year 1316?***
- Air balancing/testing, fire alarm testing and building systems commissioning continues...
- Kitchen equipment installation continues...
- Fencing, Roof Gutters, Downspouts, and Landscaping installations continue...
- Covered Play construction continues...
 - Climbing/Play Structure and game line installations has begun...
- Northwest Gymnasium Wing:
 - Rubberized and Non-Slip Flooring installation has been accelerated..
 - Climbing Wall installation pending...

Previous Relevant Status Items:

- Planning, Education Specifications, Design, Permitting, Tree Harvesting, Stump Grinding, Silt Fence Installation, Off-Site Hauling Operations, Rock/Gravel Haul-In Operations, Sanitary Sewer, Storm Drainage, Water System, On-Site Surface Water Sediment Pond, Building Slab, Parking Lots, Playgrounds, Slope Sub-Grades, Water Connection to City System, transition from the Phase 1 to Phase 2 contractor, on-site processing of topsoil, crushed rock sub-base and asphalted treated base in the entry, parking lots, exit, gravel access roads, slope protection, playfields, building layout batter boards, PSE temporary power, footing excavations, form work, under-slab power/data/plumbing infrastructure, spray on waterproof membrane, footing insulation, under-slab roll out sheet membrane, concrete building slab, ice & water shield roofing underlayment, spray on batt insulation, main PSE power, HVAC Mechanical Mezzanines, truss/sheathing roofing, exterior/interior air barrier installation/sealants, exterior flashing/weather wrap, PSE Gas Meter, exterior metal windows, masonry, capstone, acoustical wall panels, wainscoting, acoustical ceilings, ceiling grid, casework, restroom tile, exterior/interior hollow metal doors/frames, basketball equipment, gymnasium partition screen, fire sprinkler system, HVAC equipment, fire alarm, clock, data wiring, building automation systems, sidewalks, curb, gutters, entry/driveways/parking lots asphalt, **paint striping, gymnasium floor, media center/library books, and teacher boxes delivery complete...**

Future Activities: Exterior: Light poles/Lights - Flagpole - Site Furnishings - Bicycle Racks - Entry Control Gates - Exterior Signage - Final AHJ Building Inspections

**Interior: Operable Walls - Interior Signage - Library Books
Temporary Certificate of Occupancy**

Attachments:


8/10/2016 Progress Photos

**Snoqualmie Valley SD No. 410
Timber Ridge Elementary**


**Pictures Taken: 8/10/2016 - 11:30 a.m.
Progress Photographs**



Entry Plaza From Arrival Parking Lot

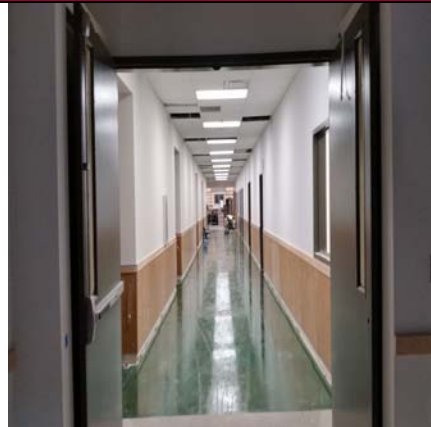

Magic Moisture Flooring Preparation

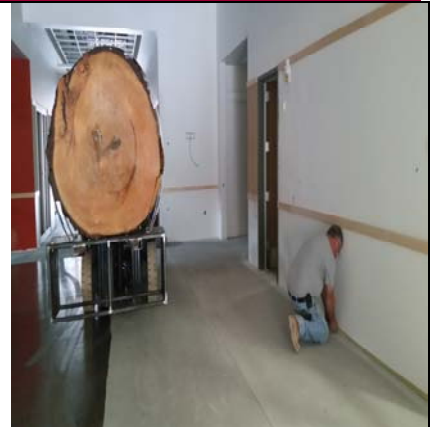

700 Year Old Feature Log Round Arrives



Music Room Ceiling And Window Install



The Media Center Book Install In Process



Gym Ready For Operable Wall Install



Gym Restrooms Pending Flooring & Stalls



Covered Play - Walkway - Upper Siding



Parking Lot Striping - Entry Plaza



Disabled Area - Walkway - Wheel Stops



Car Pool Parking - Directional Signage



Phase 1 Stockpile Going Into Landscape
