

SVSD 2015 Bond Program

Timber Ridge Elementary Progress Status Report

Date: August 19th, 2016
To: Ryan Stokes
Copy: Carolyn Malcolm, Joel Aune
From: Clint Marsh
Subject: **August 5th Current Progress Status**

Week August 12th to August 19th, as follows:

New:

Phase 2 - Building Construction

- Temporary Certificate Of Occupancy for teacher room setup issued for 8/22/2016...
- Final window installations nearing completion after being accelerated due to glazier strike...
- Air balancing/testing, fire alarm testing and building systems commissioning continues...
- Kitchen equipment installation continues...
- Fencing, Roof Gutters, Downspouts, and Landscaping installations continue...
- Climbing/Play Structure and game line installations continue...
- Northwest Gymnasium Wing:
 - Rubberized and Non-Slip Flooring installation continues...
 - Climbing Wall installation pending...

Previous Relevant Status Items:

- Planning, Education Specifications, Design, Permitting, Tree Harvesting, Stump Grinding, Silt Fence Installation, Off-Site Hauling Operations, Rock/Gravel Haul-In Operations, Sanitary Sewer, Storm Drainage, Water System, On-Site Surface Water Sediment Pond, Building Slab, Parking Lots, Playgrounds, Slope Sub-Grades, Water Connection to City System, transition from the Phase 1 to Phase 2 contractor, on-site processing of topsoil, crushed rock sub-base and asphalted treated base in the entry, parking lots, exit, gravel access roads, slope protection, playfields, building layout batter boards, PSE temporary power, footing excavations, form work, under-slab power/data/plumbing infrastructure, spray on waterproof membrane, footing insulation, under-slab roll out sheet membrane, concrete building slab, ice & water shield roofing underlayment, spray on batt insulation, main PSE power, HVAC Mechanical Mezzanines, truss/sheathing roofing, exterior/interior air barrier installation/sealants, exterior flashing/weather wrap, PSE Gas Meter, exterior metal windows, masonry, capstone, acoustical wall panels, wainscoting, acoustical ceilings, ceiling grid, casework, restroom tile, exterior/interior hollow metal doors/frames, basketball equipment, gymnasium partition screen, fire sprinkler system, HVAC equipment, fire alarm, clock, data wiring, building automation systems, sidewalks, curb, gutters, entry/driveways/parking lots asphalt, paint striping, gymnasium floor, media center/library books, teacher boxes delivery, **exterior lights/light poles, and library books complete...**

Future Activities: Exterior: Flagpole - Site Furnishings - Bicycle Racks - Entry Control Gates - Exterior Signage

Interior: Operable Walls - Interior Signage

Attachments:

8/17/2016 Progress Photos

**Snoqualmie Valley SD No. 410
Timber Ridge Elementary**


**Pictures Taken: 8/17/2016 - 11:30 a.m.
Progress Photographs**



Footing Holes For Climbing/Play Toy



Climbing/Play Toy Under Covered Roof

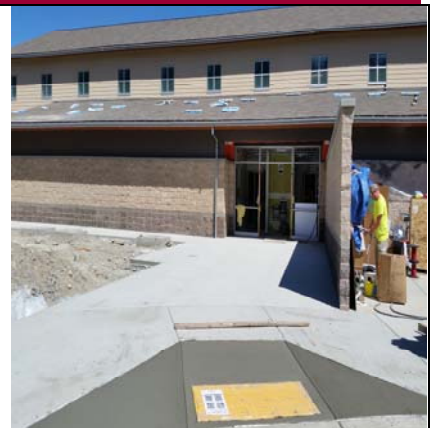

Last ADA Access At Main Gym Entrance



Main Entrance "Tree" - Post Structure



Main Entrance From Entry Vestibule



Topsoil - Irrigation - Shrubs - Fencing



Safety Stair Railings In Process



Topsoil Relocation At 50% And Climbing



One Of Many On-Site Relocation Piles



Light Poles Up - More Trees Pending



Multi-Purpose View Under Stage Lighting



Stage Pending Final Wood Trim Framing
